

Functionality Assessment of Household Tap Connection under National Jal Jeevan Mission - 2022



District Report: Arwal, Bihar Survey Duration: February to April 2022

## Contents

Abbi	reviations	3
Glos	sary	4
1.	Factsheet	6
2.	Context	8
2.1.	District snapshot: Arwal	8
2.2.	FHTC Assessment Objectives	9
2.3.	Assessment Methodology	9
2.4.	Sample Size	9
2.5.	Sampling Methodology	. 10
2.6.	Methodology for Water Quantity Measurement at Households	. 11
2.7.	Methodology for Water Quality Measurement	. 11
2.8.	Project implementation	. 12
2.9.	Sample coverage	. 13
2.10	. Sampled village and household profile	. 13
3.	Findings	. 14
3.1.	Functionality status of FHTC at household level	. 14
3.2.	Quantity, Regularity, and Quality of Water	. 15
3.3.	Average water supply days in a week	. 18
3.4.	Household utilization of water for drinking and other activities	. 18
3.5.	Status at HH level (N <sub>h</sub> =497)	. 18
3.6.	Source sustainability at the village level	. 19
3.7.	Water quality monitoring and surveillance in the villages	. 20
3.8.	Status of JJM	. 20
3.9.	Perception of HHs on Outcome Indicators	. 21
3.10	User satisfaction	. 22
4.	Annexures	. 23
4.	1. Summary of villages	. 23
4.2	2. Functionality – 55 LPCD vs regularity vs potability vs working tap connection	. 23
4.3	3. Villages not meeting the quality parameters	24



## Abbreviations



## Glossary

- 1. Community Group of people living in one particular area or village/habitation
- Cross-sectional research A cross-sectional study is a type of research design in which data is collected from a relatively large and diverse group of people at a single point in time
- 3. **Drinking water source** Groundwater (open well, borewell, tube well, handpump, spring, etc.)/ surface water (river, lake, pond, reservoir, etc.)/rainwater, available for drinking and domestic use
- 4. Improved sources The following sources as considered improved by the National Family Health Survey definitions: Piped water into dwelling, yard/plot with a tap, piped water connected to public stand-posts, tube well or borewell, Hand pump, dug well– protected, Spring–protected, Rainwater, Water ATM/ Community RO plant/ Community Water Purification Plant (CWPP)
- 5. **Unimproved sources** The following sources as considered unimproved by the National Family Health Survey definitions: Unprotected spring, unprotected dug well, cart with small tank / drum, Tanker/ truck, Surface water (river/ dam/ lake/ pond/ canal), and bottled water
- 6. **Functional Household Tap Connection (FHTC)** A tap connection to a rural household for providing drinking water in adequate quantity of prescribed quality on regular basis.
- 7. **Functionality of FHTC** Functionality of a tap connection is defined as having infrastructure, i.e., household tap connection providing water in adequate quantity, as presented:

Definitions	Fully-functional	Partially-functional	Non-functional
Quantity	>= 55 LPCD	> 40 lpcd - < 55 LPCD	< 40 LPCD
Regularity	12 months or daily basis	9-12 months or < daily basis	< 9 months or < daily basis
Quality	Potable	Potable	Non potable

- 8. **Quantity (in litres)** of water received by households per person per day should meet the service level of 55 LPCD
- 9. **Functionality Assessment** An assessment of the functionality of rural household tap connections based on a sample survey
- 10. **Fully Regular –** Regularity of water is considered when a rural household receives water for 12 months on daily basis or as per schedule.
- 11. **Potability –** Potable water is water that is safe to be used as drinking water. Parameters of potable water are mentioned below:

Parameters for potable water tested in the survey				Permissible Limit in the absence of alternative sources
i.	pH (tested on site)	-	6.5 to 8.5	No relaxation
ii.	Free residual chlorine (tested on site)	Mg/litre	0.2	1
iii.	Turbidity	NTU	1	5
iv.	Total hardness	Mg/litre	200	600
٧.	Total alkalinity	Mg/litre	200	600
vi.	Chloride	Mg/litre	250	1,000
vii.	Ammonia	Mg/litre	0.5	No relaxation
viii.	Phosphate	Mg/litre	0.3	1
ix.	Iron (in hotspots only)	Mg/litre	1	No relaxation
х.	Nitrate	Mg/litre	45	No relaxation
xi.	Sulphate	Mg/litre	200	400
xii.	Total dissolved solids	Mg/litre	500	2,000
xiii.	Fluoride	Mg/litre	1	1.5



xiv.	Arsenic (in hotspots only)	Mg/litre	0.01	No relaxation
XV.	Bacteriological test for Total bacteria and E. coli or therm coliform bacteria		Shall not be detectable in any	100 ml sample

- 12. **Sampling** Selection of a subset of individuals from within a statistical population to estimate water service delivery among the population. In the current study, households have been sampled to estimate the representation of the village and subsequently of the district as well as of the state.
- 13. Types of schemes: Following are the piped water supply schemes that were assessed
  - a. Mini-solar based piped water supply scheme in isolated/tribal hamlets
  - b. Single Village Scheme (SVS) in villages having adequate groundwater that needs treatment
  - c. Single village scheme (having adequate groundwater/ spring water/ local or surface water source of prescribed Quality)
  - Retrofitting of ongoing schemes taken up under erstwhile NRDWP for the last mile connectivity/ retrofitting of completed rural water supply schemes to make it JJM compliant
  - e. Multi-village PWS scheme with water grids/ regional water supply schemes
- 14. Village Action Plan (VAP) Plan prepared by Gram Panchayat and/ or its sub-committee, i.e., VWSC/ Paani Samiti/ User Group, etc. based on baseline survey, resource mapping and felt needs of the village community to provide FHTC to every rural household, treat the generated greywater and plan its reuse, undertake surveillance activities, etc. VAP also indicates the fund requirement and timelines for completion of work under the Mission and will be approved by the Gram Sabha. Irrespective of the source of funding, all drinking water-related works in the village are taken up based on the VAP.
- 15. **Source Sustainability** includes measures such as aquifer recharge, rainwater harvesting, increased storage capacity of water bodies, reservoirs, de-silting, etc. improve the lifespan of water supply systems
- 16. Har Ghar Jal (HGJ) An administrative unit wherein all HHs are provided with water supply through FHTCs is called "Har Ghar Jal".
- 17. **Public Institutions** The public institutions in the survey include Aanganwadi Centre (AWC), Health Facilities, Schools, Gram Panchayat, and government buildings.
- 18. Working tap connection A tap connection supplied water at least one day in the week, preceding of survey
- **19. Functional Scheme –** A scheme is said to be functional if it was reported to be working for all 12 months in a year.



## 1. Factsheet

Table 1: District level factsheet

Functionality status of FHTC at households Households (HHs) which received water through FHTC at least once in last 7 days (%) Fully functional (%) Partially functional (%) Non-functional (%) Quantity of water received by households Adequate quantity (>55 LPCD) (%) Partially adequate quantity (>40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%) Regularity of water received by households	89 78 20 2 97 1 2	55 74 22 4 93 3 3
7 days (%) Fully functional (%) Partially functional (%) Non-functional (%) Quantity of water received by households Adequate quantity (>55 LPCD) (%) Partially adequate quantity (>40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	78 20 2 97 1	74 22 4 93 3
Fully functional (%) Partially functional (%) Non-functional (%) Quantity of water received by households Adequate quantity (>55 LPCD) (%) Partially adequate quantity (>40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	20 2 97 1	22 4 93 3
Partially functional (%) Non-functional (%) Quantity of water received by households Adequate quantity (>55 LPCD) (%) Partially adequate quantity (>40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	20 2 97 1	22 4 93 3
Non-functional (%) Quantity of water received by households Adequate quantity (>55 LPCD) (%) Partially adequate quantity (> 40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	2 97 1	4 93 3
Quantity of water received by households Adequate quantity (>55 LPCD) (%) Partially adequate quantity (> 40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	97 1	93
Adequate quantity (>55 LPCD) (%) Partially adequate quantity (> 40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	1	3
Partially adequate quantity (> 40 LPCD - < 55 LPCD) (%) Inadequate quantity (<40 LPCD) (%)	1	3
Inadequate quantity (<40 LPCD) (%)	•	
	2	1
Regularity of water received by households	2	4
Fully Regular Supply (as per schedule) (%)	84	78
Partially Regular Supply (not as per schedule) (%)	9	11
Irregular Supply (less than 9 months' supply) (%)	7	11
Potable (Quality) water received by households		
Potable (%)	94	99
Non-potable (%)	6	1
Residual Chlorine (RCL) detected with in permissible limits (%)	5	1

Household level indicators		
Households receiving water supply daily-7 days a week (%)	97	84
Daily HH requirement of water being met by FHTC (%)	73	47
Households reported FHTC as a primary source of drinking water (%)	59	31
Households purifying water before drinking (%)	11	8
Households paying water service delivery charges (%)	6	7
Households having coping mechanisms during scarcity (%)	14	22
Households aware of grievance redressal mechanism for reporting	65	51
problems with FHTC (%)		
Households reported incidence of water-borne diseases in the last year (%)	0	1
Households reported a reduction in time and effort in collecting water (%)	86	31
Overall user satisfaction at the household level		
Regularity (%)	89	69
Overall quality (%)	88	68




Indicators	Bihar	Arwal
Village level indicators (based on village questionnaire)		
Schemes reported to be functional (%)	38	40
Villages with groundwater resource (%)	26	6
Villages having groundwater recharge structure <sup>1</sup> (%)	9	0
Water supply and storage status in villages		
Average no. of times water is supplied in a day	2	2
Villages having OHT/ Sump for storage of water (%)	80	41
Water quality monitoring and surveillance in the villages		
Villages with Field Test Kits (%)	13	6
Villages in which bacteriological test was done in last 1 year by VWSC/	21	0
Pani Samiti (%)		
Villages reported to have a mechanism for chlorination (%)	26	0
VWSC/Pani Samiti and PWS signage in villages		
Village reported having presence of VWSC/ Pani Samiti (%)	23	3
Villages in which VWSC/ Pani Samiti is responsible for Operation & Maintenance of PWS schemes (%)	7	0
Villages in which persons are trained to use Field Test Kits (%)	14	3
Villages in which signages about JJM were observed (%)	30	0
Operation and maintenance at village		
Villages levying water service delivery to households (%)	5	3
Convergence of JJM activities with other schemes in the villages (%)	3	0
Villages having skilled manpower for Operation & Maintenance of PWS	31	0
schemes (%)		
Community monitoring of water wastage in villages (%)	11	0

 $<sup>^{1}</sup>$  Out of villages who reported to have groundwater source (N\_v=2)

## 2. Context

Jal Jeevan Mission (JJM) was launched on the 15th of August 2019 with the objective to provide functional household tap connections (FHTCs) to all rural households.

Figure 1: Har Ghar Jal - Objective, Vision, & Outcome



In accordance with the overall objectives as specified in the Operational Guidelines for the implementation of the NJJM, Gol carried out a sample survey to assess the functionality of household tap connections. As part of this endeavour, NJJM, Gol engaged HTA Kantar Public to conduct the 'Functionality Assessment' of the household as well as public institution/ buildings such as schools, anganwadis, gram panchayat buildings, public health facilities, and wellness centers in all the rural districts for the fiscal year 2021-22.

## 2.1. District snapshot: Arwal

District Arwal of Bihar has a population of 7,78,440. The district has 5 blocks. Out of 339 villages in the district, 27 are SC dominated and 1 are ST dominated villages. The district lies in Lower Gangetic Plains Region and receives an annual rainfall of 722.6mm.

Presented here are district level information collated from the DDWS-IMIS:

Figure 1: District IMIS Status & Map

#### IMIS status:


- 337 (99% of all) villages are Har Ghar Jal
- 2 (1% of all) villages are non-Har ghar Jal
- Non-SC/ST dominated district
- Non-JE/AES
- No- History of water contamination
- 337 (99% of all) villages with PWS more than 20 FHT(





## 2.2. FHTC Assessment Objectives


Figure 3: Objectives of Functionality of Tap Connections

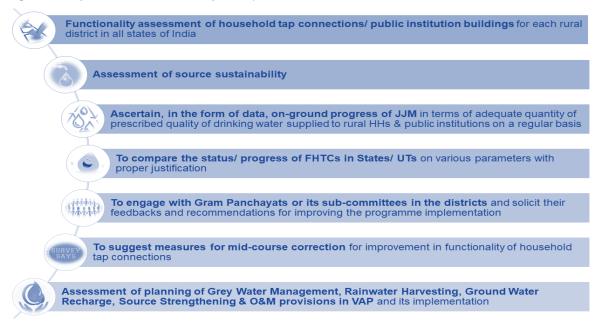

## 2.3. Assessment Methodology

A cross-section research design has been used for this functionality assessment study. Quantitative data were collected from villages and households across all states/UTs using the CAPI (Computer Assisted Personal Interviewing) mode. The survey includes two components, village, and household.

Figure 4: Survey Components & Respondents

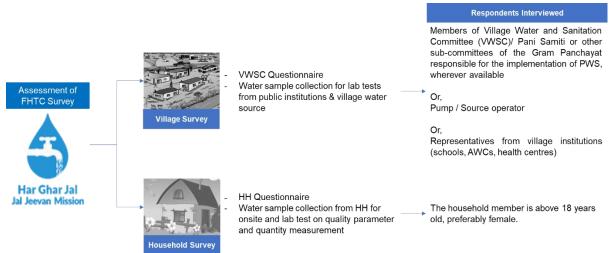

## 2.4. Sample Size

The sample size was calculated to provide estimates with a 95% confidence interval (CI) and 5% margin of error (MoE) after incorporating the correction factor for a finite population considering the total number of geographic units having FHTCs.

- Village sample is estimated to be representative at the state level
- HH sample estimated to be representative at the district level



- Number of Har Ghar Jal (HGJ) villages were proportionately sampled at the district level
- All PWS schemes (up to 4) were covered per village. Per scheme approximately 9 (3 each from the head, middle, and tail HHs) or 18 households (6 each from head, middle, and tail HHs) were sampled to achieve the desired sample at the district level.

## 2.5. Sampling Methodology

As per the design, all villages having a PWS scheme with 20 or more functional household tap connections were included in the sample frame. The probability proportionate to size (PPS) method was used for village selection in each district. The steps for random selection of villages using PPS are as presented:

Figure 5: Steps for Village Sampling



The key considerations for the village and household sampling were:

Figure 2: Sampling Considerations – Village & Households



The record of all district-wise village replacements is maintained and reported as part of the annexure.

## 2.6. Methodology for Water Quantity Measurement at Households

Figure 7: Steps for Measuring Flowrate from Supply-tap at HHs



The flow rate of the water supply was measured using a container with gradual markings (either 5 litres or 1 litre, based on the flow of the tap) and a stopwatch/timer-watch. The process followed is as described in Figure 7.

In the case of households where the FHTC is connected directly with the storage tank, the following steps were adopted to measure the quantity:

- Assessor first asked and recorded length, breadth, and height.
- Assessor dipped a 5 feet long rod, marked the level of the water table, and calculated the volume – length x breadth x-height of water.
- Next the assessor opened the valve of the connection and allowed the water to flow inside the storage for 10 minutes.
- After 10 mins, the valve was closed, and the assessor again dipped the rod and recorded the new height of the water inside the tank. Based on this new 'height' and the CAPI calculated the changed volume.
- The difference in the volume of water in 10 minutes divided by 10 provided the flow rate of the water supply per minute.


The water flow rate was not measured for village-level public institutions.

## 2.7. Methodology for Water Quality Measurement

Water quality was tested for all public institutions available in the villages, including schools, anganwadis, gram panchayat buildings, public health facilities, and wellness centers, and at the selected households. Two types of quality tests were carried out – a) spot test for pH and free residual chlorine, and b) water sample was collected and transported to labs for testing against 13 quality parameters (total 15) as specified in Figure 8.



#### Figure 8: On-site & Laboratory Based Quality Test

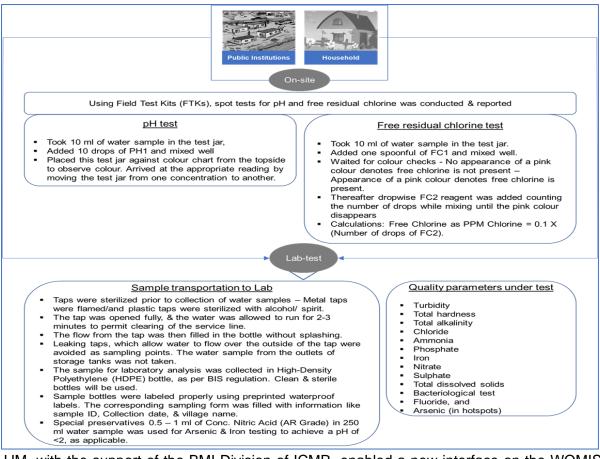

JJM, with the support of the BMI Division of ICMR, enabled a new interface on the WQMIS portal for "Functionality Assessment (FA) User" to enable seamless harmonization of water sample registration, sample submission for testing, and sharing of results as per the applicable quality parameters.

## 2.8. Project implementation

An overview of the project implementation is as presented:

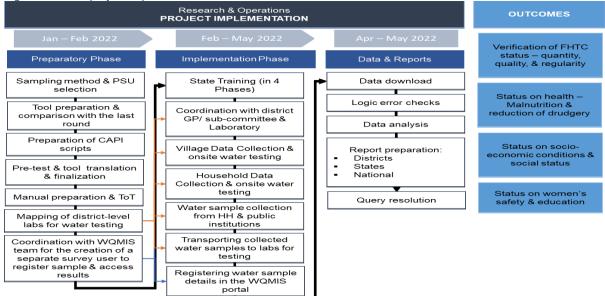


Figure 9: Broad project implementation framework



A total of 15 teams (comprising 15 supervisors, 90 assessors, and 15 water collection assistants) were recruited, trained, and deployed to complete the survey across the states of Bihar. One survey team covered approximately 2 - 3 districts. The state-wise team deployment and fieldwork dates were as presented:

Table No. 1:	State-wise team deployment and data collection start & end dates				
State		Teams deployed	Start date	End date	Total data collection days
Bihar		15 Teams	02-18-2022	04-02-2022	42 days

A four-tier quality control (QC) system was put in place. At the ground level, the data collection exercise was done using a computer-aided Personal Interview (CAPI) application which contained all logic and skip-checks inbuilt. Also, 5% of the total samples were accompanied by the supervisors. Sub-targeted QC was done by the state field managers (5%) and the central project management team (5%). Apart from this, the central research team monitored the data trend and as per requirement debriefed data collection teams to improve quality.

## 2.9. Sample coverage

Table No. 2:	Table No. 2: Sample covered				
	Targetee	d sample		Achieved sam	ple
District	Village	НН	Village	НН	Public Institutions
Arwal	32	495	32	497	11
Bihar	812	16,308	812	16,404	318

## 2.10. Sampled village and household profile

SAMPLED VILLAGES	SAMPLED HOUSEHOLDS
Total no. of villages covered in the district – 32	Total no. of households covered in the district
Percentage of SC dominated villages covered	- 274
in the district is 0% (which is lower than the	• Proportion of General - 19%, SC 22%, ST% 2,
state average, i.e., 11%)	OBC 58% households
Percentage of ST dominated villages covered	• 34% of the FHTC connections are under the
in the district is 0% (which is lower than the	name of a female member
state average, i.e., 2%)	<ul> <li>Average household size – 7</li> </ul>
Higher proportion of pump operator	<ul> <li>&gt;75% positive user experience in 0/5</li> </ul>
interviewed at the village level	measures
No, the district reported to have any historical	
incidence of water contamination	



## 3. Findings

## 3.1. Functionality status of FHTC at household level



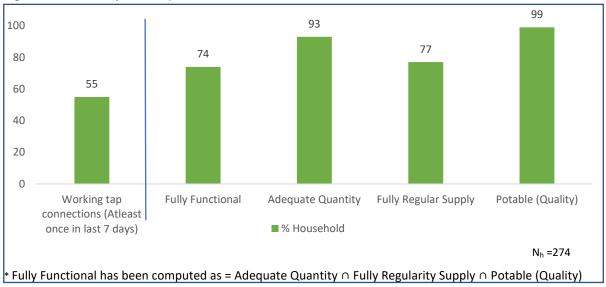


Figure 3: Functionality of HH tap connection

It has been found that 55 percent of the sampled HHs (N=274) had working tap connections (i.e., received water at least once in last 7 days). More than 2 out of 10 (74 percent) HHs had fully functional tap connection (i.e., HHs receiving adequate quantity of prescribed quality of water on a regular basis).




## 3.2. Quantity, Regularity, and Quality of Water

Under JJM, functionality is defined as having infrastructure, i.e., household tap connection providing water in adequate quantity (55 LPCD or more) of prescribed quality on regular basis (every day or as decided by GP and/ or its sub-committee) with adequate pressure. It will also include long-term source and system sustainability. Presented here are the findings in this respect.

#### A. Water quantity measured as LPCD (Litres per Capita per Day)


93% HHs reported receiving adequate quantity of water

Figure 4: Quantity of water received by households



#### Quantity of water received across head, middle, and tail end HHs


Figure 5: Quantity of water received across head, middle and tail end households




#### B. Regularity of water supply to households

### **78% HHs** receive a regular supply of water (as per agreed schedule)


Figure: Regularity of water received by households












#### C. Water quality - Potability

Figure 7: Potable water received by households



\*Potable water has been considered basis testing of water samples through laboratory tests for physical, chemical, and bacteriological as given in Table 4 parameters (within acceptable/permissible range) and onsite testing of pH. The details of laboratory test are mentioned in the table given above in the glossary.

Table No. 3:	Village quality parameters reported within permissible range (% sample
within per	rmissible range)

	Water Samples Tested from Public Institutes					
Quality Parameters (NV=32)	Anganwadi Centre	Health Facility	Schools	Others		
pH (on-site)	100		100	100		
Turbidity	100		100	100		
Total Hardness	100		100	100		
Total Alkalinity	100		100	100		
Chloride	Not tested					
Ammonia		Not t	ested			
Iron		No hi	istory			
Nitrate	100		100	100		
Sulphate	100		100	100		
Total Dissolved Solids	100		100	100		
Bacteriological Test	Not tested					



Fluoride	No history
Arsenic	No history

#### Table No. 4: Household water quality parameters reported within permissible range (in % sample within permissible range)

Quality Parameters	No of samples tested	% Households			
pH (on-site)	274	99			
Turbidity	266	100			
Total Hardness	264	100			
Total Alkalinity	266	100			
Chloride	Not tested				
Ammonia	Not tested				
Iron	No history				
Nitrate	265	100			
Sulphate	264	100			
Total Dissolved Solids	266	100			
Bacteriological Test (Presence/Absence)	Not tested				
Fluoride	No history				
Arsenic	No history				

#### Safeguarding piped water supply for unforeseen bacteriological contamination-Presence of Residual Chlorine (RC)

The Residual Chlorine (RC) in the Arwal district was found in 1% samples. Out of which 0% samples were having RC outside range whereas 99% samples, had no RC.

The Residual Chlorine in piped water supply is one of the most important preventive actions to assure quality of water against bacteriological contamination from source to consumption. The presence of residual chlorine within permissible limits is indicator of well-maintained and healthy piped water supply system.

It is advised that behavioural change communication campaigns on appropriate dosage of residual chlorine is held in all villages and monitoring system for chlorine dosing is established. The FTK must have residual chlorine testing facility for effective WQM&S.

#### **Comment on functioning of District Lab:**


The district lab tested water samples for 6 water quality parameters. 285 water samples were submitted, and 275 water samples were tested, and reports made available. The turnaround time for testing was more than 48 hours in most cases.

The labs did not have capacity to test more than 40 number of samples and had issues of human resource, regents etc




## 3.3. Average water supply days in a week






## 3.4. Household utilization of water for drinking and other activities

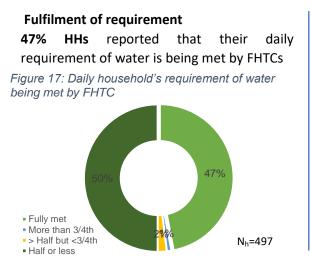


## 3.5. Status at HH level (Nh=497)

## Primary source of drinking water31% HHs reported HH tap connection as their

primary source of drinking water Figure 18: Households reported FHTC as primary source of drinking water



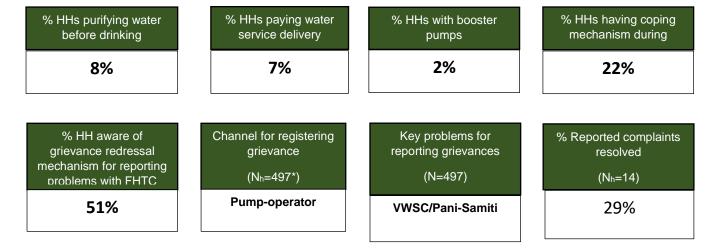


\*HHs who reported complaints in last 1 year

## 3.6. Source sustainability at the village level

#### Schemes based on surface and ground water

0% of schemes are reported to be based on surface water and 4% ground water.


Figure 19: Schemes based on water source in village




\*'Surface Water Source' is Stream, Spring, Glacier, River, lake, pond etc. and Groundwater Source is open well, borewell, tube well, handpump, spring, etc

#### Villages reported having presence of a groundwater source

**6% of villages** reported the presence of groundwater sources like improved dug wells and borewells, and were supported by recharging structures.





#### The top 3 other source sustainability measure taken by villages

Figure 21: Villages reported having taken other source sustainability measure





## 3.7. Water quality monitoring and surveillance in the villages

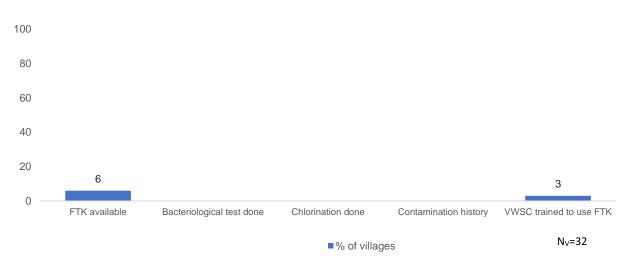


Figure 22: Water quality monitoring and surveillance by villages

## 3.8. Status of JJM

## A. VWSC/Pani Samiti and PWS signage in villages ( $N_v=32$ )

Presence of VWSC/Pani Samiti	VWSC/Pani Samiti responsible for O&M of	% Villages – VWSC/PO trained to use FTKs	% Villages with PWS signages
3%	0%	3%	0%

## B. Water supply, storage and operation & maintenance at village level (Nv=32)

Average no. of supply in a day	% Villages levying water service delivery to HH	% Villages with skilled manpower for O&M	Community monitoring of water wastage in villages
2	3%	0%	0%
% Villages having OHT/ Sump	% Villages having faced O&M challenges	Primary points for reporting grievances	Key problems for reporting grievances
41%	0%	Block functionary	Pipeline leakage




## 3.9. Perception of HHs on Outcome Indicators

#### a. Health


#### Incidence of water borne diseases at HH level in last one year as reported

Figure 23: Household reported incidence of water borne diseases in last one year




#### b. Economic Income Change in employment days since FHTC programmes/schemes

Figure 24: Household reported a change in employment days since FHTC programmes /schemes



#### c. Drudgery Reduction in time and effort in collecting water

Figure 25: Households reported reduction in time and effort in collecting water





## 3.10. User satisfaction

Table No.	Table No. 5:         User satisfaction - more than 75% happy with FHTC services					
S. No.	Parameter (N <sub>h</sub> =497)	In %				
1	Regularity	( <u></u>	69			
2	Overall quality	(Pero)	68			
3	Colour	( <u></u> , •)	70			
4	Taste	( <u>e</u> )	69			
5	Odour		70			

Note:

Base ( $N_v$ )=32 means all villages sampled and covered in Arwal district

Base (N<sub>H</sub>)=497 means all households sampled and covered across the 32 villages in Arwal district Base (N<sub>H</sub>)=497 means all households where female members used to fetch water before HH tap connection



## 4. Annexures

## 4.1. Summary of villages

Table No						
S.No.	Name of sample village	Sample HHs	Actual sample HHs (achieved)	No. of scheme	No of source of surface water	No of source of Ground water
1	Total	495	529	27	1	4
2	Ibrahimpur	9	10	1		
3	Pinjranwan	27	28	1		
4	Dhondar	9	11	1		
5	Bara	18	19	1		
6	Rajepur	9	10	1		
7	Anuan	9	10	1	1	
8	Dharampur	9	10	1		
9	Khatangi	18	19	1		
10	Kutubpur Tera	27	27	1		
11	Sarmastpur Newana	9	10	0		
12	Rasulpur Pariyari	9	10	1		
13	Chauhar	18	19	1		
14	Kochahsa	27	28	0		3
15	Jonha	9	8	1		
16	Rampurchae	18	19	1		
17	Shahar Telpa	18	19	1		
18	Karpi	27	32	1		
19	Kasauti	9	10	1		
20	Aiyara	27	29	0		
21	Durgapur	9	10	1		
22	Parasrampur	9	10	0		
23	Masuda	36	37	1		
24	Agnur	27	27	1		
25	Jaipur	18	19	1		
26	Teri	9	10	1		
27	Feinku Bigha	9	10	1		
28	Nasirpur Sarwar	9	10	1		
29	Sarauti	18	19	1		
30	Etawan	9	10	1		
31	Fatepur Sanda	9	10	1		
32	Mardan Vigha	9	10	1		
33	Makhmilpur	18	19	0		1

# 4.2. Functionality – 55 LPCD vs regularity vs potability vs working tap connection

Table	Table No. 7: Functionality of HH tap connection						
S. No.	Village	Fully Functional* (% HH)	Adequate Quantity (% HH)	Fully Regular Supply (% HH)	Potable (Quality) (% HH)	Working tap connections (%HH)	
1	Total	73	93	77	98	100	
2	Ibrahimpur	56	100	56	100	100	
3	Pinjranwan	73	100	82	91	100	
4	Dhondar	100	100	100	100	100	
5	Bara	100	100	100	100	100	
6	Rajepur	100	100	100	100	100	
7	Anuan	20	100	20	100	100	
8	Dharampur	0	100	0	100	100	
9	Khatangi	73	100	73	100	100	
10	Kutubpur Tera	44	67	67	100	100	



11	Chauhar	94	100	100	94	100
12	Kochahsa	0	11	0	100	100
13	Rampurchae	0	0	80	80	100
14	Shahar Telpa	50	83	50	100	100
15	Karpi	70	100	74	96	100
16	Kasauti	50	100	50	100	100
17	Aiyara	83	100	83	100	100
18	Masuda	70	70	90	100	100
19	Agnur	82	100	82	100	100
20	Jaipur	78	100	89	89	100
21	Teri	89	100	89	100	100
22	Feinku Bigha	0	100	0	100	100
23	Nasirpur					
	Sarwar	67	100	67	100	100
24	Sarauti	85	100	85	100	100
25	Etawan	89	100	89	100	100
26	Fatepur Sanda	100	100	100	100	100
27	Makhmilpur	100	100	100	100	100

\* Fully Functional has been computed as = Adequate Quantity  $\cap$  Fully Regularity Supply  $\cap$  Potable (Quality)

#### Villages not meeting the quality parameters 4.3.

Table		ble Quality paramete	ers dissatisfied	at village level	
1. pł	I (Acceptable	Range- 6.5 to 8.5)			
S.No.	Block Name	Panchayat Name	Villages	No. of HHs outside the acceptab	le range
1	Kaler	Jaipur	Jaipur		1
2		Pinjrawa	Pinjranwan		1
2. Fr	ee residual cl	hlorine (Acceptable I	Range- 0.2 to 1	PPM)	-
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	HHs with no chlorine
1	Arwal	Abgila	Etawan	0	9
2		Bhadasi	Feinku Bigha	0	6
3	-	Khabhaini	Nasirpur Sarwar	0	9
4		Rampur Vaina	Fatepur Sanda	0	9
5		Sarauti	Sarauti	0	13
6	Kaler	Jaipur	Jaipur	0	8
7		Kaler South	Agnur	0	17
8		Sakrikhurd	Masuda	0	10
9		Teri	Teri	0	9
10	Karpi	Aiyara	Aiyara	0	12
11		Bambhai	Kasauti	0	6
12		Chouhar	Chauhar	0	18
13		Durra	Kutubpur Tera	0	9
14		Karpi	Karpi	0	23
15		Kochhasa	Kochahsa	0	9
16		Rampur Chai	Rampurchae	0	5
17		Shahartelpa	Shahar Telpa	0	6
18	Kurtha	Bara	Bara	0	17
19	]	Ibrahim Pur	Ibrahimpur	0	9
20	]	Kodmarai	Dhondar	0	10
21	]	Manik Pur	Rajepur	0	9
22		Pinjrawa	Pinjranwan	0	11
23	Sonbhadra	Anuaa	Anuan	0	5
24	Banshi	Chamandi	Dharampur	0	4
25	]	Khatangi	Khatangi	0	11
26		Sher Pur	Makhmilpur	0	18
3. Tu	Irbidity (Acce	ptable Range- 1 to 5	NTU)		




Table No. 8:       Table Quality parameters dissatisfied at village level         S.No.       Block Name       Panchayat Name       Villages       HHs outside the acceptation							
	able/permissible range						
NA NA NA NA							
4. Total hardness (Acceptable Range- 200 to 600 Milligram/litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
5. Total alkalinity (Acceptable Range- 200 to 600 Milligram/litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
6. Chloride (Acceptable Range- 250 to 1000 Milligram/litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
7. Ammonia (Acceptable Range- 0.5 Milligram/litre)							
S.No. Block Name Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
8. Iron (Acceptable Range- 1 Milligram/litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
1 Karpi Chouhar Chauhar	1						
9. Nitrate (Acceptable Range- 1 Milligram/litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
10. Sulphate (Acceptable Range- 200 to 400 Milligram/litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
1 Karpi Rampur Chai Rampurchae	1						
11. Total dissolved solids (Acceptable Range- 500 to 2000 Milligram/litre)							
S.No. Block Name Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
12. Bacteriological test (Presence)							
S.No. Block Name Panchayat Name Villages HHs outside the accepta	ble/permissible range						
NA NA NA NA							
13. Fluoride (Acceptable Range- 1 to 1.5 Milligram /litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						
1 Karpi Karpi Karpi	1						
14. Arsenic (in hotspots) (Acceptable Range- 0.01 Milligram /litre)							
S.No. Block Panchayat Name Villages HHs outside the accepta	ble/permissible range						

