



Functionality Assessment of Household Tap Connection under National Jal Jeevan Mission - 2022



**District Report: Dang, Gujarat
Survey Duration: February to March 2022**

Contents

Abbreviations	3
Glossary	4
1. Factsheet.....	6
2. Context	8
2.1. District snapshot: Dang	8
2.2. FHTC Assessment Objectives	9
2.3. Assessment Methodology	9
2.4. Sample Size	9
2.5. Sampling Methodology.....	10
2.6. Methodology for Water Quantity Measurement at Households	11
2.7. Methodology for Water Quality Measurement	11
2.8. Project implementation.....	12
2.9. Sample coverage	13
2.10. Sampled village and household profile	13
3. Findings.....	14
3.1. Functionality status of FHTC at household level.....	14
3.2. Quantity, Regularity, and Quality of Water.....	15
3.3. Average water supply days in a week.....	18
3.4. Household utilization of water for drinking and other activities	18
3.5. Status at HH level (Nh=398)	18
3.6. Source sustainability at the village level	19
3.7. Water quality monitoring and surveillance in the villages	20
3.8. Status of JJM.....	20
3.9. Perception of HHs on Outcome Indicators.....	21
3.10. User satisfaction.....	22
4. Annexures	23
4.1. Summary of villages.....	23
4.2. Functionality – 55 LPCD vs regularity vs potability vs working tap connection	23
4.3. Villages not meeting the quality parameters	24

Abbreviations

AWC	Aanganwadi Centre
FHTC	Functional Household Tap Connection
GoI	Government of India
GP	Gram Panchayat
HF	Health Facility
HH	Household
HGJ	Har Ghar Jal
JJM	Jal Jeevan Mission
LPCD	Litres per Capita per Day
MVS	Multi-village Scheme
NJJM	National Jal Jeevan Mission
RC	Residual Chlorine
O&M	Operation and Maintenance
OHT	Over Head Tank
PSU	Primary Sampling Unit
PWS	Piped Water Supply
SVS	Single Village Scheme
VAP	Village Action Plan
VWSC	Village Water and Sanitation Committee
WQMIS	Water Quality Monitoring and Information System

Glossary

1. **Community** – Group of people living in one particular area or village/habitation
2. **Cross-sectional research** – A cross-sectional study is a type of research design in which data is collected from a relatively large and diverse group of people at a single point in time
3. **Drinking water source** – Groundwater (open well, borewell, tube well, handpump, spring, etc.)/ surface water (river, lake, pond, reservoir, etc.)/rainwater, available for drinking and domestic use
4. **Improved sources** – The following sources as considered improved by the National Family Health Survey definitions: Piped water into dwelling, yard/plot with a tap, piped water connected to public stand-posts, tube well or borewell, Hand pump, dug well–protected, Spring–protected, Rainwater, Water ATM/ Community RO plant/ Community Water Purification Plant (CWPP)
5. **Unimproved sources** – The following sources as considered unimproved by the National Family Health Survey definitions: Unprotected spring, unprotected dug well, cart with small tank / drum, Tanker/ truck, Surface water (river/ dam/ lake/ pond/ canal), and bottled water
6. **Functional Household Tap Connection (FHTC)** – A tap connection to a rural household for providing drinking water in adequate quantity of prescribed quality on regular basis.
7. **Functionality of FHTC** – Functionality of a tap connection is defined as having infrastructure, i.e., household tap connection providing water in adequate quantity, as presented:

Definitions	Fully-functional	Partially-functional	Non-functional
Quantity	≥ 55 LPCD	> 40 lpcd - < 55 LPCD	< 40 LPCD
Regularity	12 months or daily basis	9-12 months or $<$ daily basis	< 9 months or $<$ daily basis
Quality	Potable	Potable	Non potable

8. **Quantity (in litres)** of water received by households per person per day should meet the service level of 55 LPCD
9. **Functionality Assessment** – An assessment of the functionality of rural household tap connections based on a sample survey
10. **Fully Regular** – Regularity of water is considered when a rural household receives water for 12 months on daily basis or as per schedule.
11. **Potability** – Potable water is water that is safe to be used as drinking water. Parameters of potable water are mentioned below:

Parameters for potable water tested in the survey	Unit	Acceptable Limit	Permissible Limit in the absence of alternative sources
i. pH (tested on site)	-	6.5 to 8.5	No relaxation
ii. Free residual chlorine (tested on site)	Mg/litre	0.2	1
iii. Turbidity	NTU	1	5
iv. Total hardness	Mg/litre	200	600
v. Total alkalinity	Mg/litre	200	600
vi. Chloride	Mg/litre	250	1000
vii. Ammonia	Mg/litre	0.5	No relaxation
viii. Phosphate	Mg/litre	0.3	1
ix. Iron (in hotspots only)	Mg/litre	1	No relaxation
x. Nitrate	Mg/litre	45	No relaxation
xi. Sulphate	Mg/litre	200	400
xii. Total dissolved solids	Mg/litre	500	2000
xiii. Fluoride	Mg/litre	1	1.5

xiv.	Arsenic (in hotspots only)	Mg/litre	0.01	No relaxation
xv.	Bacteriological test for Total coliform bacteria and E. coli or thermotolerant coliform bacteria	Shall not be detectable in any 100 ml sample		

12. **Sampling** – Selection of a subset of individuals from within a statistical population to estimate water service delivery among the population. In the current study, households have been sampled to estimate the representation of the village and subsequently of the district as well as of the state.
13. **Types of schemes:** Following are the piped water supply schemes that were assessed
 - a. Mini-solar based piped water supply scheme in isolated/tribal hamlets
 - b. Single Village Scheme (SVS) in villages having adequate groundwater that needs treatment
 - c. Single village scheme (having adequate groundwater/ spring water/ local or surface water source of prescribed Quality)
 - d. Retrofitting of ongoing schemes taken up under erstwhile NRDWP for the last mile connectivity/ retrofitting of completed rural water supply schemes to make it JJM compliant
 - e. Multi-village PWS scheme - with water grids/ regional water supply schemes
14. **Village Action Plan (VAP)** – Plan prepared by Gram Panchayat and/ or its sub-committee, i.e., VWSC/ Paani Samiti/ User Group, etc. based on baseline survey, resource mapping and felt needs of the village community to provide FHTC to every rural household, treat the generated greywater and plan its reuse, undertake surveillance activities, etc. VAP also indicates the fund requirement and timelines for completion of work under the Mission and will be approved by the Gram Sabha. Irrespective of the source of funding, all drinking water-related works in the village are taken up based on the VAP.
15. **Source Sustainability** – includes measures such as aquifer recharge, rainwater harvesting, increased storage capacity of water bodies, reservoirs, de-silting, etc. improve the lifespan of water supply systems
16. **Har Ghar Jal (HGJ)** – An administrative unit wherein all HHs are provided with water supply through FHTCs is called “Har Ghar Jal”.
17. **Public Institutions** – The public institutions in the survey include Aanganwadi Centre (AWC), Health Facilities, Schools, Gram Panchayat, and government buildings.
18. **Working tap connection** – A tap connection supplied water at least one day in the week, preceding of survey
19. **Functional Scheme** – A scheme is said to be functional if it was reported to be working for all 12 months in a year.

1. Factsheet

Table 1: District level factsheet

Indicators	State	District
Functionality status of FHTC at households		
Households (HHs) which received water through FHTC at least once in last 7 days (%)	99	100
Fully functional (%)	71	95
Partially functional (%)	21	3
Non-functional (%)	8	1
Quantity of water received by households		
Adequate quantity (>55 LPCD) (%)	87	97
Partially adequate quantity (> 40 LPCD - < 55 LPCD) (%)	5	2
Inadequate quantity (<40 LPCD) (%)	8	1
Regularity of water received by households		
Fully Regular Supply (as per schedule) (%)	88	100
Partially Regular Supply (not as per schedule) (%)	7	0
Irregular Supply (less than 9 months' supply) (%)	5	0
Potable (Quality) water received by households		
Potable (%)	89	99
Non-potable (%)	11	1
Residual Chlorine (RCL) detected with in permissible limits (%)	50	30
Household level indicators		
Households receiving water supply daily-7 days a week (%)	73	100
Daily HH requirement of water being met by FHTC (%)	93	99
Households reported FHTC as a primary source of drinking water (%)	87	82
Households purifying water before drinking (%)	98	97
Households paying water service delivery charges (%)	88	98
Households having coping mechanisms during scarcity (%)	29	24
Households aware of grievance redressal mechanism for reporting problems with FHTC (%)	96	97
Households reported incidence of water-borne diseases in the last year (%)	1	0
Households reported a reduction in time and effort in collecting water (%)	94	99
Overall user satisfaction at the household level		
Regularity (%)	93	100
Overall quality (%)	95	100

Indicators	State	District
Village level indicators (based on village questionnaire)		
Schemes reported to be functional (%)	73	92
Villages with groundwater resource (%)	69	91
Villages having groundwater recharge structure ¹ (%)	7	9
Water supply and storage status in villages		
Average no. of times water is supplied in a day	2	1
Villages having OHT/ Sump for storage of water (%)	92	100
Water quality monitoring and surveillance in the villages		
Villages with Field Test Kits (%)	80	100
Villages in which bacteriological test was done in last 1 year by VWSC/ Pani Samiti (%)	77	100
Villages reported to have a mechanism for chlorination (%)	19	9
VWSC/Pani Samiti and PWS signage in villages		
Village reported having presence of VWSC/ Pani Samiti (%)	89	100
Villages in which VWSC/ Pani Samiti is responsible for Operation & Maintenance of PWS schemes (%)	42	64
Villages in which persons are trained to use Field Test Kits (%)	78	100
Villages in which signages about JJM were observed (%)	64	45
Operation and maintenance at village		
Villages levying water service delivery to households (%)	87	100
Convergence of JJM activities with other schemes in the villages (%)	31	0
Villages having skilled manpower for Operation & Maintenance of PWS schemes (%)	61	55
Community monitoring of water wastage in villages (%)	53	18

¹ Out of villages who reported to have groundwater source (N_v=10)

2. Context

Jal Jeevan Mission (JJM) was launched on the 15th of August 2019 with the objective to provide functional household tap connections (FHTCs) to all rural households.

Figure 1: Har Ghar Jal - Objective, Vision, & Outcome



In accordance with the overall objectives as specified in the Operational Guidelines for the implementation of the NJJM, GoI carried out a sample survey to assess the functionality of household tap connections. As part of this endeavour, NJJM, GoI engaged HTA Kantar Public to conduct the 'Functionality Assessment' of the household as well as public institution/ buildings such as schools, anganwadis, gram panchayat buildings, public health facilities, and wellness centers in all the rural districts for the fiscal year 2021-22.

2.1. District snapshot: Dang


District Dang of Gujarat has a population of 228224. The district has 3 blocks. Out of 303 villages in the district, 13 are SC dominated and 289 are ST dominated villages. The district lies in Gujarat Plains and Hills Region and receives an annual rainfall of 2226.8mm.

Presented here are district level information collated from the DDWS-IMIS:

Figure 2: District IMIS Status & Map

IMIS status:

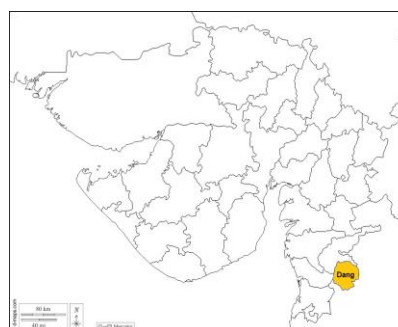- 280 (92% of all) villages are Har Ghar Jal
- 23 (8% of all) villages are Non-Har ghar Jal
- SC/ST dominated district
- Non JE/AES
- Yes- History of water contamination
- 303 (1% of all) villages with PWS more than 20 FHTC;



2.2. FHTC Assessment Objectives

Figure 3: Objectives of Functionality of Tap Connections



2.3. Assessment Methodology

A cross-section research design has been used for this functionality assessment study. Quantitative data were collected from villages and households across all states/UTs using the CAPI (Computer Assisted Personal Interviewing) mode. The survey includes two components, village, and household.

Figure 4: Survey Components & Respondents



2.4. Sample Size

The sample size was calculated to provide estimates with a 95% confidence interval (CI) and 5% margin of error (MoE) after incorporating the correction factor for a finite population considering the total number of geographic units having FHTCs.

- Village sample is estimated to be representative at the state level
- HH sample estimated to be representative at the district level

- Number of Har Ghar Jal (HGJ) villages were proportionately sampled at the district level
- All PWS schemes (up to 4) were covered per village. Per scheme approximately 9 (3 each from the head, middle, and tail HHs) or 18 households (6 each from head, middle, and tail HHs) were sampled to achieve the desired sample at the district level.

2.5. Sampling Methodology

As per the design, all villages having a PWS scheme with 20 or more functional household tap connections were included in the sample frame. The probability proportionate to size (PPS) method was used for village selection in each district. The steps for random selection of villages using PPS are as presented:

Figure 5: Steps for Village Sampling



The key considerations for the village and household sampling were:

Figure 6: Sampling Considerations – Village & Households



The record of all district-wise village replacements is maintained and reported as part of the annexure.

2.6. Methodology for Water Quantity Measurement at Households

Figure 7: Steps for Measuring Flowrate from Supply-tap at HHs



The flow rate of the water supply was measured using a container with gradual markings (either 5 litres or 1 litre, based on the flow of the tap) and a stopwatch/timer-watch. The process followed is as described in Figure 7.

In the case of households where the FHTC is connected directly with the storage tank, the following steps were adopted to measure the quantity:

- Assessor first asked and recorded length, breadth, and height.
- Assessor dipped a 5 feet long rod, marked the level of the water table, and calculated the volume – length x breadth x-height of water.
- Next the assessor opened the valve of the connection and allowed the water to flow inside the storage for 10 minutes.
- After 10 mins, the valve was closed, and the assessor again dipped the rod and recorded the new height of the water inside the tank. Based on this new 'height' and the CAPI calculated the changed volume.
- The difference in the volume of water in 10 minutes divided by 10 provided the flow rate of the water supply per minute.

The water flow rate was not measured for village-level public institutions.

2.7. Methodology for Water Quality Measurement

Water quality was tested for all public institutions available in the villages, including schools, anganwadis, gram panchayat buildings, public health facilities, and wellness centers, and at the selected households. Two types of quality tests were carried out – a) spot test for pH and free residual chlorine, and b) water sample was collected and transported to labs for testing against 13 quality parameters (total 15) as specified in Figure 8.

Figure 8: On-site & Laboratory Based Quality Test



JJM, with the support of the BMI Division of ICMR, enabled a new interface on the WQMIS portal for “Functionality Assessment (FA) User” to enable seamless harmonization of water sample registration, sample submission for testing, and sharing of results as per the applicable quality parameters.

2.8. Project implementation

An overview of the project implementation is as presented:

Figure 9: Broad project implementation framework



A total of 10 teams (comprising 10 supervisors, 60 assessors, and 10 water collection assistants) were recruited, trained, and deployed to complete the survey across the state of Gujarat. One survey team covered approximately 2 – 3 districts. The state-wise team deployment and fieldwork dates were as presented:

Table No. 1: State-wise team deployment and data collection start & end dates				
State	Teams deployed	Start date	End date	Total data collection days
Gujarat	10 Teams	2/15/2022	3/25/2022	35 Days

A four-tier quality control (QC) system was put in place. At the ground level, the data collection exercise was done using a computer-aided Personal Interview (CAPI) application which contained all logic and skip-checks inbuilt. Also, 5% of the total samples were accompanied by the supervisors. Sub-targeted QC was done by the state field managers (5%) and the central project management team (5%). Apart from this, the central research team monitored the data trend and as per requirement debriefed data collection teams to improve quality.

2.9. Sample coverage

Table No. 2: Sample covered					
District	Targeted sample		Achieved sample		
	Village	HH	Village	HH	Public Institutions
Dang	11	378	11	398	28
Gujarat	384	13,104	384	13,716	1,018

2.10. Sampled village and household profile


SAMPLED VILLAGES	SAMPLED HOUSEHOLDS
<ul style="list-style-type: none"> Total no. of villages covered in the district – 11 Percentage of SC dominated villages covered in the district is 9% (which is higher than the state average, i.e., 1%) Percentage of ST dominated villages covered in the district is 91% (which is higher than the state average, i.e., 30%) Higher proportion of pump operator interviewed at the village level Yes the district reported to have any historical incidence of water contamination 	<ul style="list-style-type: none"> Total no. of households covered in the district – 398 Proportion of General - 1%, SC 0%, ST% 99, OBC 1% households 6% of the FHTC connections are under the name of a female member Average household size – 6 >75% positive user experience in 5/5 measures

3. Findings

3.1. Functionality status of FHTC at household level

A. Overall Functionality* (in %)

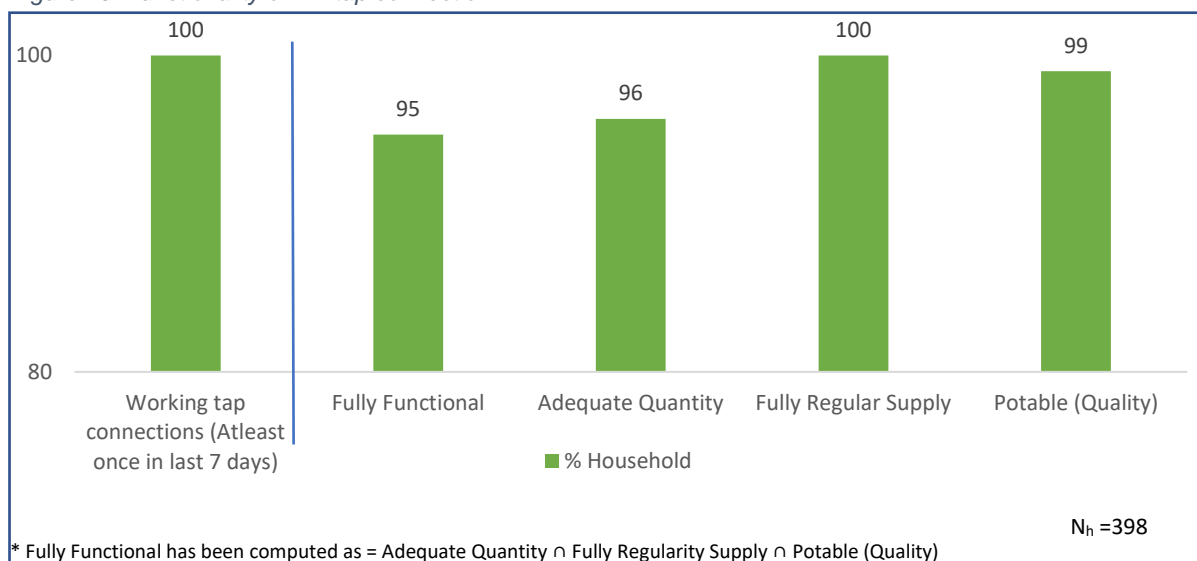Figure 10: Functionality of HH tap connection



It has been found that 100 percent of the sampled HHs (N=398) had working tap connections (i.e., received water at least once in last 7 days). More than nine out of ten (95 percent) HHs had fully functional tap connection (i.e., HHs receiving adequate quantity of prescribed quality of water on a regular basis).


3.2. Quantity, Regularity, and Quality of Water

Under JJM, functionality is defined as having infrastructure, i.e., household tap connection providing water in adequate quantity (55 LPCD or more) of prescribed quality on regular basis (every day or as decided by GP and/ or its sub-committee) with adequate pressure. It will also include long-term source and system sustainability. Presented here are the findings in this respect.

A. Water quantity measured as LPCD (Litres per Capita per Day)


96% HHs reported receiving adequate quantity of water

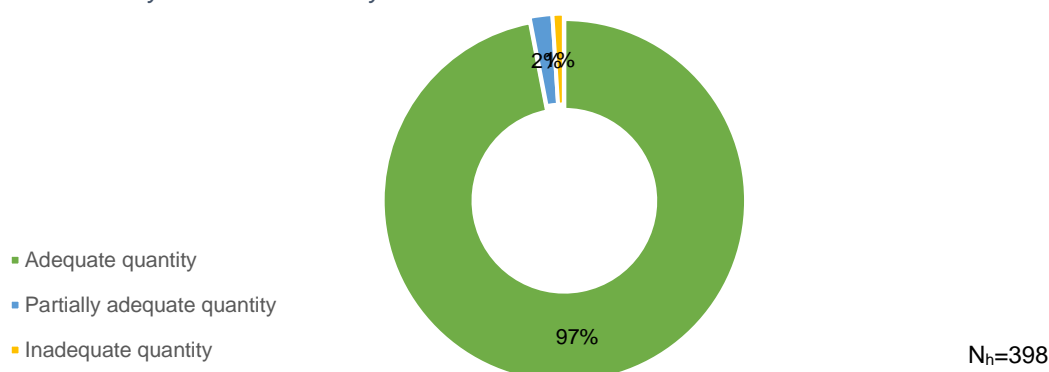Figure 11: Quantity of water received by households



Quantity of water received across head, middle, and tail end HHs

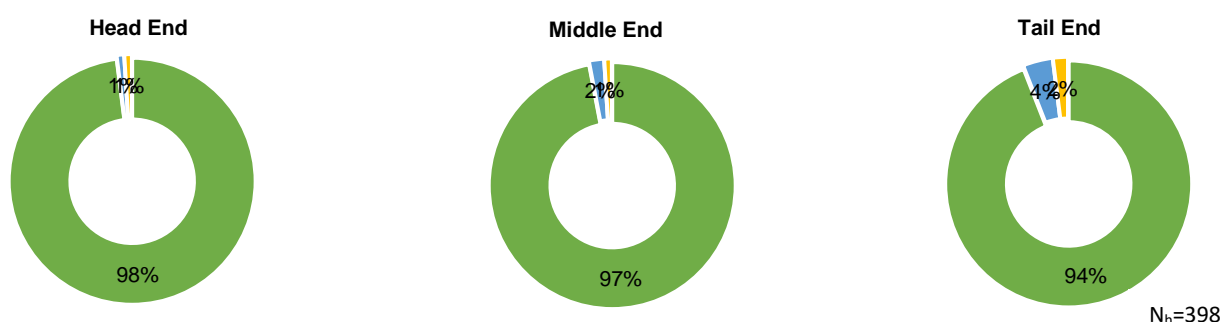
Figure 12: Quantity of water received across head, middle and tail end households



B. Regularity of water supply to households


100% HHs receive a regular supply of water (as per agreed schedule)

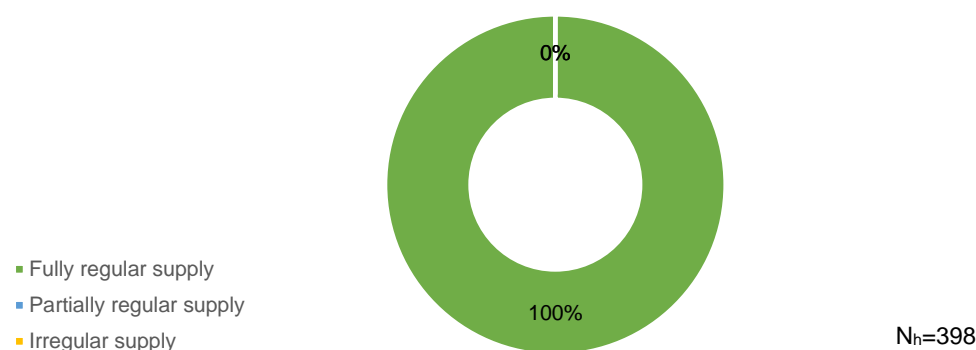Figure: Regularity of water received by households




Regularity of water received across head, middle, and tail end

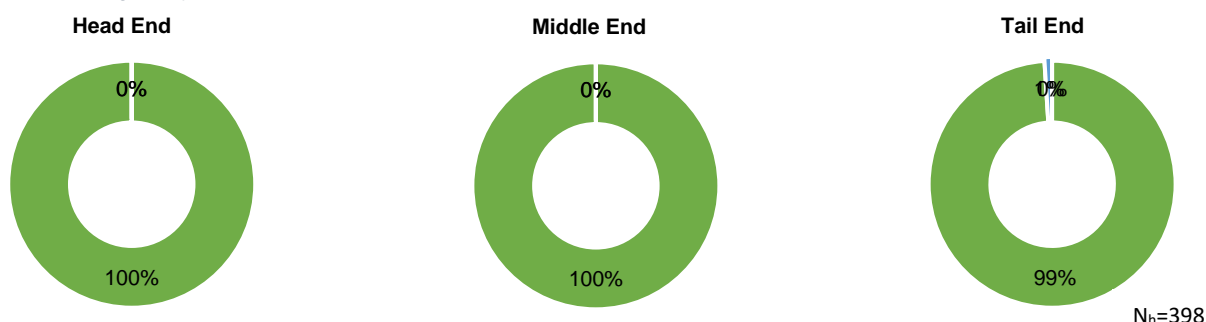Figure 13: Regularity of water received across head, middle and tail end households



C. Water quality – Potability

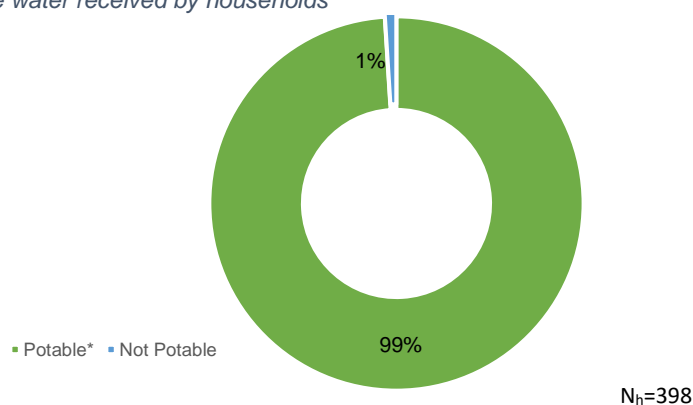Figure 14: Potable water received by households



*Potable water has been considered basis testing of water samples through laboratory tests for physical, chemical, and bacteriological as given in Table 4 parameters (within acceptable/ permissible range) and onsite testing of pH. The details of laboratory test are mentioned in the table given above in the glossary.

Table No. 3: Village quality parameters reported within permissible range (in %)

Quality Parameters (NV=11)	Water Samples Tested from Public Institutes			
	Anganwadi Centre	Health Facility	Schools	Others
pH (on-site)	100	100	100	100
Turbidity	100	100	100	100
Total Hardness	100	100	100	100
Total Alkalinity	100	100	100	100
Chloride	100	100	100	100
Ammonia	Not tested			
Iron	Not tested			
Nitrate	100	100	100	100
Sulphate	100	100	100	100
Total Dissolved Solids	100	100	100	100
Bacteriological Test	100	100	100	100
Fluoride	No history			
Arsenic	No history			

Table No. 4: Household water quality parameters reported within permissible range (in % sample within permissible range)

Quality Parameters	No of water samples tested	% Samples within permissible range
pH (on-site)	398	100
Turbidity	385	100
Total Hardness	381	100
Total Alkalinity	383	100
Chloride	383	100
Ammonia	Not tested	
Iron	Not tested	
Nitrate	382	100
Sulphate	381	100
Total Dissolved Solids	385	100
Bacteriological Test(Presence/Absence)	380	100
Fluoride	No history	
Arsenic (In Hotspots)	No history	

Safeguarding piped water supply for unforeseen bacteriological contamination- Presence of Residual Chlorine (RC)

The Residual Chlorine (RC) in the Dang district was found in 30% samples. Out of which 0% samples were having RC outside range whereas 70% samples, had no RC. It may be mentioned that 100% of water samples passed the bacteriological contamination test but to assure the protection against bacteriological contamination, addition of RC is must in PWS system.

The Residual Chlorine in piped water supply is one of the most important preventive actions to assure quality of water against bacteriological contamination from source to consumption. The presence of residual chlorine within permissible limits is indicator of well-maintained and healthy piped water supply system.

It is advised that behavioural change communication campaigns on appropriate dosage of residual chlorine is held in all villages and monitoring system for chlorine dosing is established. The FTK must have residual chlorine testing facility for effective WQM&S.


Comment on functioning of District Lab:

The district lab tested water samples for 8 water quality parameters. 426 water samples were submitted, and 414 water samples were tested, and reports made available. The turnaround time for testing was more than 48 hours in most cases.

The labs did not have any issue with testing the number of water samples submitted nor had any issues with human resource, reagents etc

3.3. Average water supply days in a week

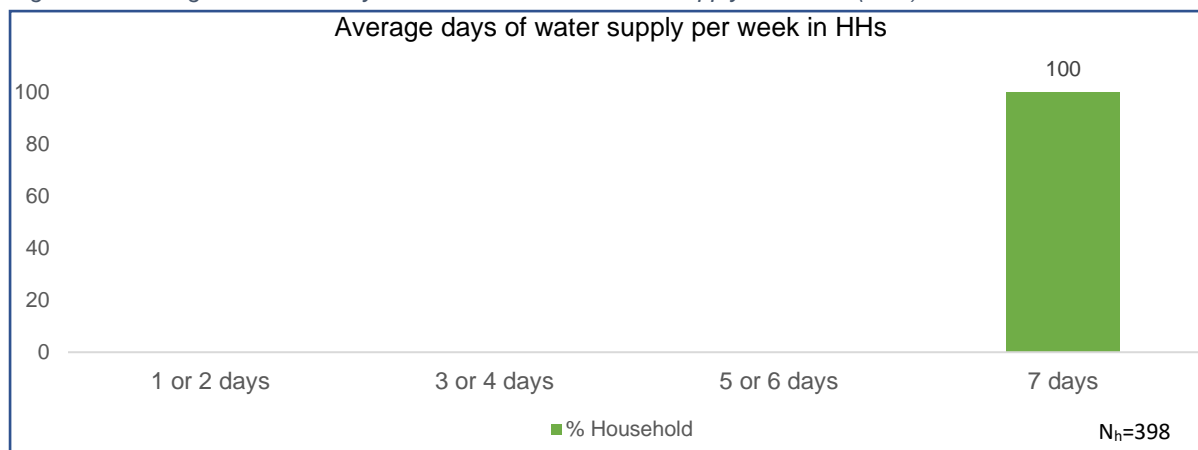Figure 15: Average number of days households receive water supply in a week (in %)




3.4. Household utilization of water for drinking and other activities

Fulfilment of requirement

99% HHs reported that their daily requirement of water is being met by FHTCs

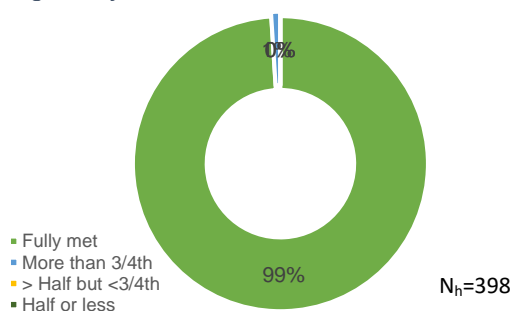
Figure 17: Daily household's requirement of water being met by FHTC



Primary source of drinking water

82% HHs reported HH tap connection as their primary source of drinking water

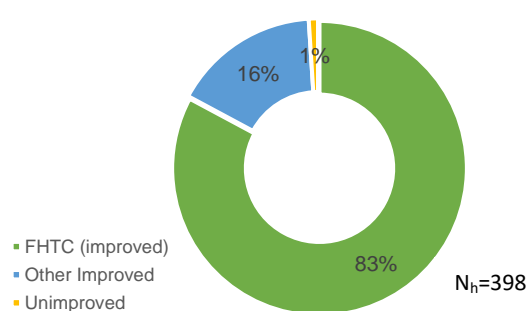Figure 18: Households reported FHTC as primary source of drinking water



3.5. Status at HH level (N_h=398)

% HHs purifying water before drinking	% HHs paying water service delivery charges	% HHs with booster pumps	% HHs having coping mechanism during scarcity
97%	98%	7%	24%
% HH aware of grievance redressal mechanism for reporting problems with FHTC	Channel for registering grievance (N _h =398*)	Key problems for reporting grievances (N=398)	% Reported complaints resolved (N _h =10)
97%	GP functionaries	Pipeline leakage	80%


*HHs who reported complaints in last 1 year

3.6. Source sustainability at the village level

Schemes based on surface and ground water

0% of schemes are reported to be based on surface water and 91% ground water.

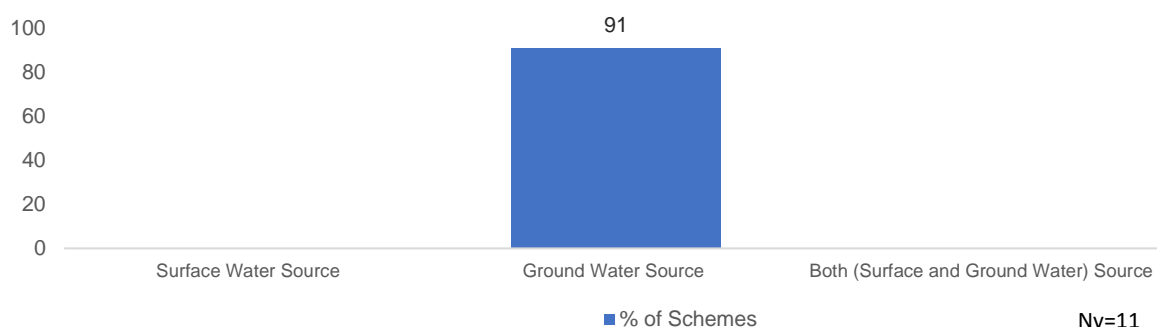Figure 19: Schemes based on water source in village




*'Surface Water Source' is Stream, Spring, Glacier, River, lake, pond etc. and Groundwater Source is open well, borewell, tube well, handpump, spring, etc

Villages reported having presence of a groundwater source

91% of villages reported the presence of groundwater sources like improved dug wells and borewells, and 9% were supported by recharging structures.

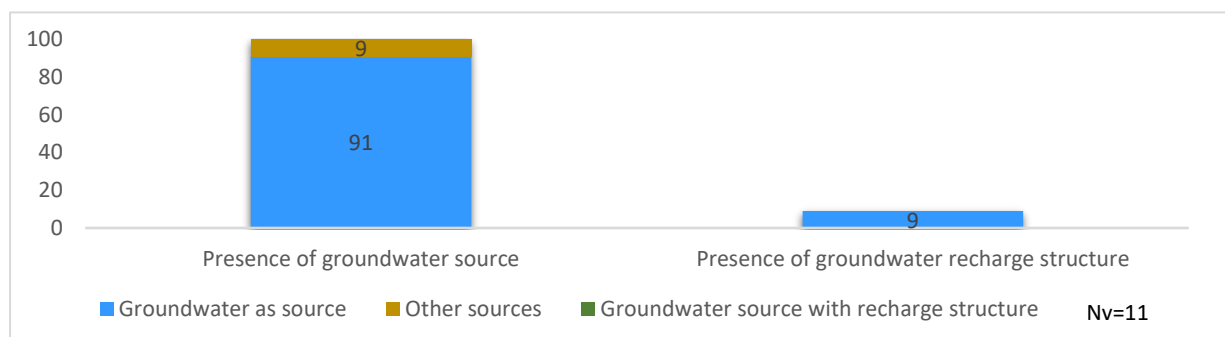Figure 20: Villages reported the presence of groundwater sources and among those how many reported to have a recharge structure




The top 3 other source sustainability measure taken by villages

Figure 21: Villages reported having taken other source sustainability measure

No source sustainability measures taken by any village in the district.

3.7. Water quality monitoring and surveillance in the villages

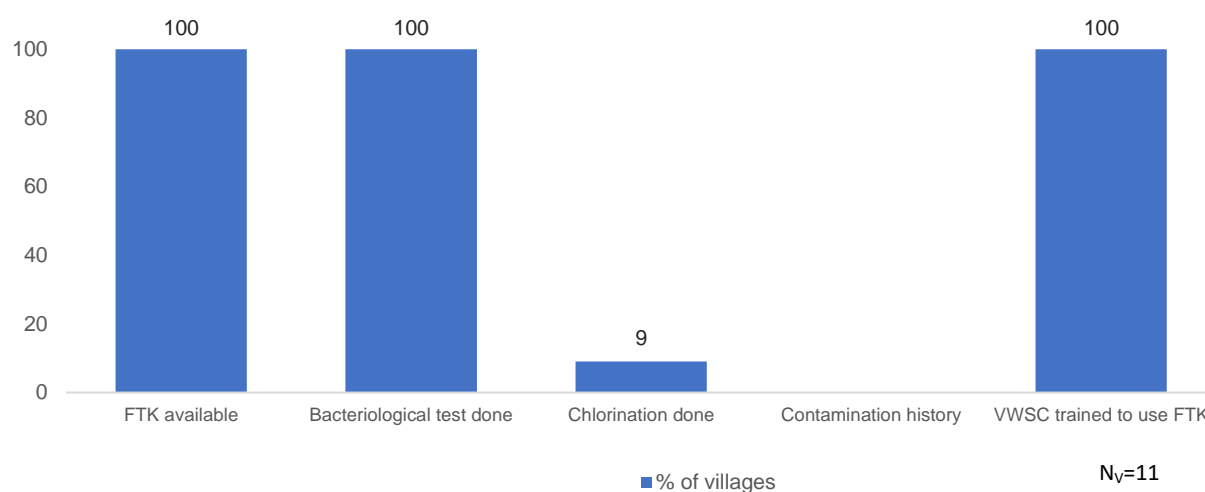Figure 22: Water quality monitoring and surveillance by villages



3.8. Status of JJM

A. VWSC/Pani Samiti and PWS signage in villages (N_v=11)

Presence of VWSC/Pani Samiti	VWSC/Pani Samiti responsible for O&M of PWS Schemes	% Villages – VWSC/PO trained to use FTKs	% Villages with PWS signages
100%	64%	100%	45%

B. Water supply, storage and operation & maintenance at village level (N_v=11)


Average no. of supply in a day	% Villages levying water service delivery to HH	% Villages having skilled manpower for O&M for PWS	Community monitoring of water wastage in villages
1	100%	55%	18%
% Villages having OHT/ Sump	% Villages with O&M challenges	Primary points for reporting grievances	Key problems for reporting grievances
100%	0%	Helpline	Pipeline leakage

3.9. Perception of HHs on Outcome Indicators

a. Health

Incidence of water borne diseases at HH level in last one year as reported

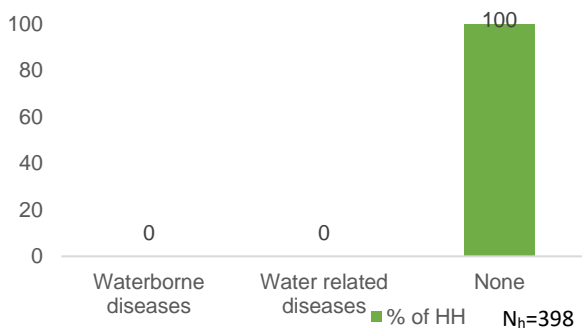
Figure 23: Household reported incidence of water borne diseases in last one year



b. Economic Income

Change in employment days since FHTC programmes/schemes

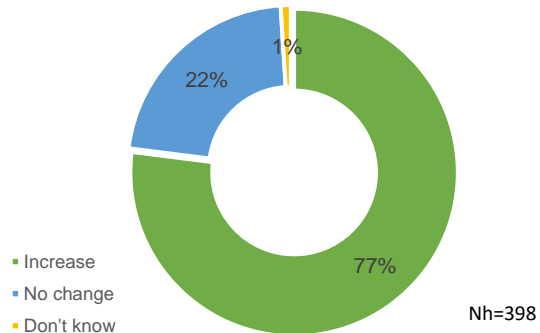
Figure 24: Household reported a change in employment days since FHTC programmes /schemes







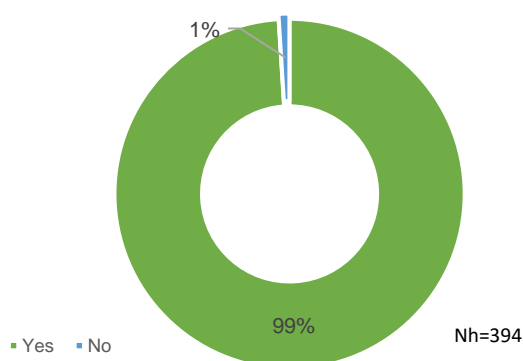
c. Drudgery

Reduction in time and effort in collecting water

Figure 25: Households reported reduction in time and effort in collecting water



3.10. User satisfaction

Table No. 5: User satisfaction - more than 75% happy with FHTC services			
S. No.	Parameter (N _H =398)		In %
1	Regularity		100
2	Overall quality		100
3	Colour		100
4	Taste		99
5	Odour		100

Note:

Base (N_V)=11 means all villages sampled and covered in Dang district

Base (N_H)=398 means all households sampled and covered across the 11 villages in Dang district

Base (N_H)=398 means all households where female members used to fetch water before HH tap connection

4. Annexures

4.1. Summary of villages

Table No. 6: Village Summary						
S.No.	Name of sample village	Sample HHs	Actual sample HHs (achieved)	No. of scheme	No of source of surface water available in the village	No of source of ground water available in the village
#	Dang	378	409	10		11
1	Kadmal(Subir)	36	37	1		1
2	Pipalyamal	36	39	0		
3	Khajurna	36	37	1		1
4	Vanzat Amba	36	39	1		1
5	Supdahad	36	37	1		1
6	Jamlapada(Gad	54	57	1		1
7	Gundvahal	36	43	1		1
8	Ambapada (Vag	18	21	1		2
9	Behdun	36	37	1		1
10	Lavariya	18	23	1		1
11	Saputara	36	39	1		1

4.2. Functionality – 55 LPCD vs regularity vs potability vs working tap connection

Table No. 7: Functionality of HH tap connection						
S. No.	Village	Functionality* (% HH)	Adequate Quantity (% HH)	Fully Regular Supply (% HH)	Potable (Quality) (% HH)	Working tap connections (%HH)
#	Dang	95	97	100	99	100
1	Kadmal(Subir)	94	94	100	100	100
2	Pipalyamal	95	100	100	95	100
3	Khajurna	100	100	100	100	100
4	Vanzat Amba	100	100	100	100	100
5	Supdahad	100	100	100	100	100
6	Jamlapada(Gad	84	84	100	100	100
7	Gundvahal	98	100	100	98	100
8	Ambapada (Vag	100	100	100	100	100
9	Behdun	94	100	97	97	100
10	Lavariya	91	91	100	100	100
11	Saputara	97	97	100	100	100

* Fully Functional has been computed as = Adequate Quantity \cap Fully Regularity Supply \cap Potable (Quality)

4.3. Villages not meeting the quality parameters

Table No. 8: Quality parameters dissatisfied at village level					
1. pH (Acceptable Range- 6.5 to 8.5)					
S.No.	Block Name	Panchayat Name	Villages	No. of HHs outside the acceptable range	
1	Waghai	Nadagchond	Gundvahal	1	
2. Free residual chlorine (Acceptable Range- 0.2 to 1 PPM)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	HHs with no chlorine
1	Ahwa	Chankhal	Pipalyamal	0	5
2		Divantembur	Jamlapada(Gad	0	46
3		Malegaw	Saputara	0	37
4	Subir	Chichvihir	Khajurna	0	36
5		Kadmal	Kadmal(Subir)	0	18
6		Pipaldahad	Behdun	0	36
7	Waghai	Bhendmal	Lavariya	0	22
8		Daguniya	Supdahad	0	23
9		Nadagchond	Gundvahal	0	20
10		Zavda	Vanzat Amba	0	37
3. Turbidity (Acceptable Range- 1 to 5 NTU)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
1	Ahwa	Chankhal	Pipalyamal	1	
4. Total hardness (Acceptable Range- 200 to 600 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
5. Total alkalinity (Acceptable Range- 200 to 600 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
6. Chloride (Acceptable Range- 250 to 1000 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
7. Ammonia (Acceptable Range- 0.5 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
8. Iron (Acceptable Range- 1 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
9. Nitrate (Acceptable Range- 1 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
10. Sulphate (Acceptable Range- 200 to 400 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
11. Total dissolved solids (Acceptable Range- 500 to 2000 Milligram/litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
NA	NA	NA	NA	NA	
12. Bacteriological test (Presence)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	
1	Ahwa	Chankhal	Pipalyamal	1	
13. Fluoride (Acceptable Range- 1 to 1.5 Milligram /litre)					
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range	

Table No. 8: Quality parameters dissatisfied at village level				
1	Subir	Pipaldahad	Behdun	1
14. Arsenic (in hotspots) (Acceptable Range- 0.01 Milligram /litre)				
S.No.	Block Name	Panchayat Name	Villages	HHs outside the acceptable/permissible range
NA	NA	NA	NA	NA
